Updated project schedule

Sideline | Implementation snapshot: October 11, 2026

Planning snapshot: October 11, 2026. The exact December deadline remains unconfirmed. Dates below are proposed work windows, not completed activities or professor requirements.

Completed: source audit, SQL store, baseline, advanced features, model, web app, local automated checks and screenshot capture. Documentation and slides accompany this package.

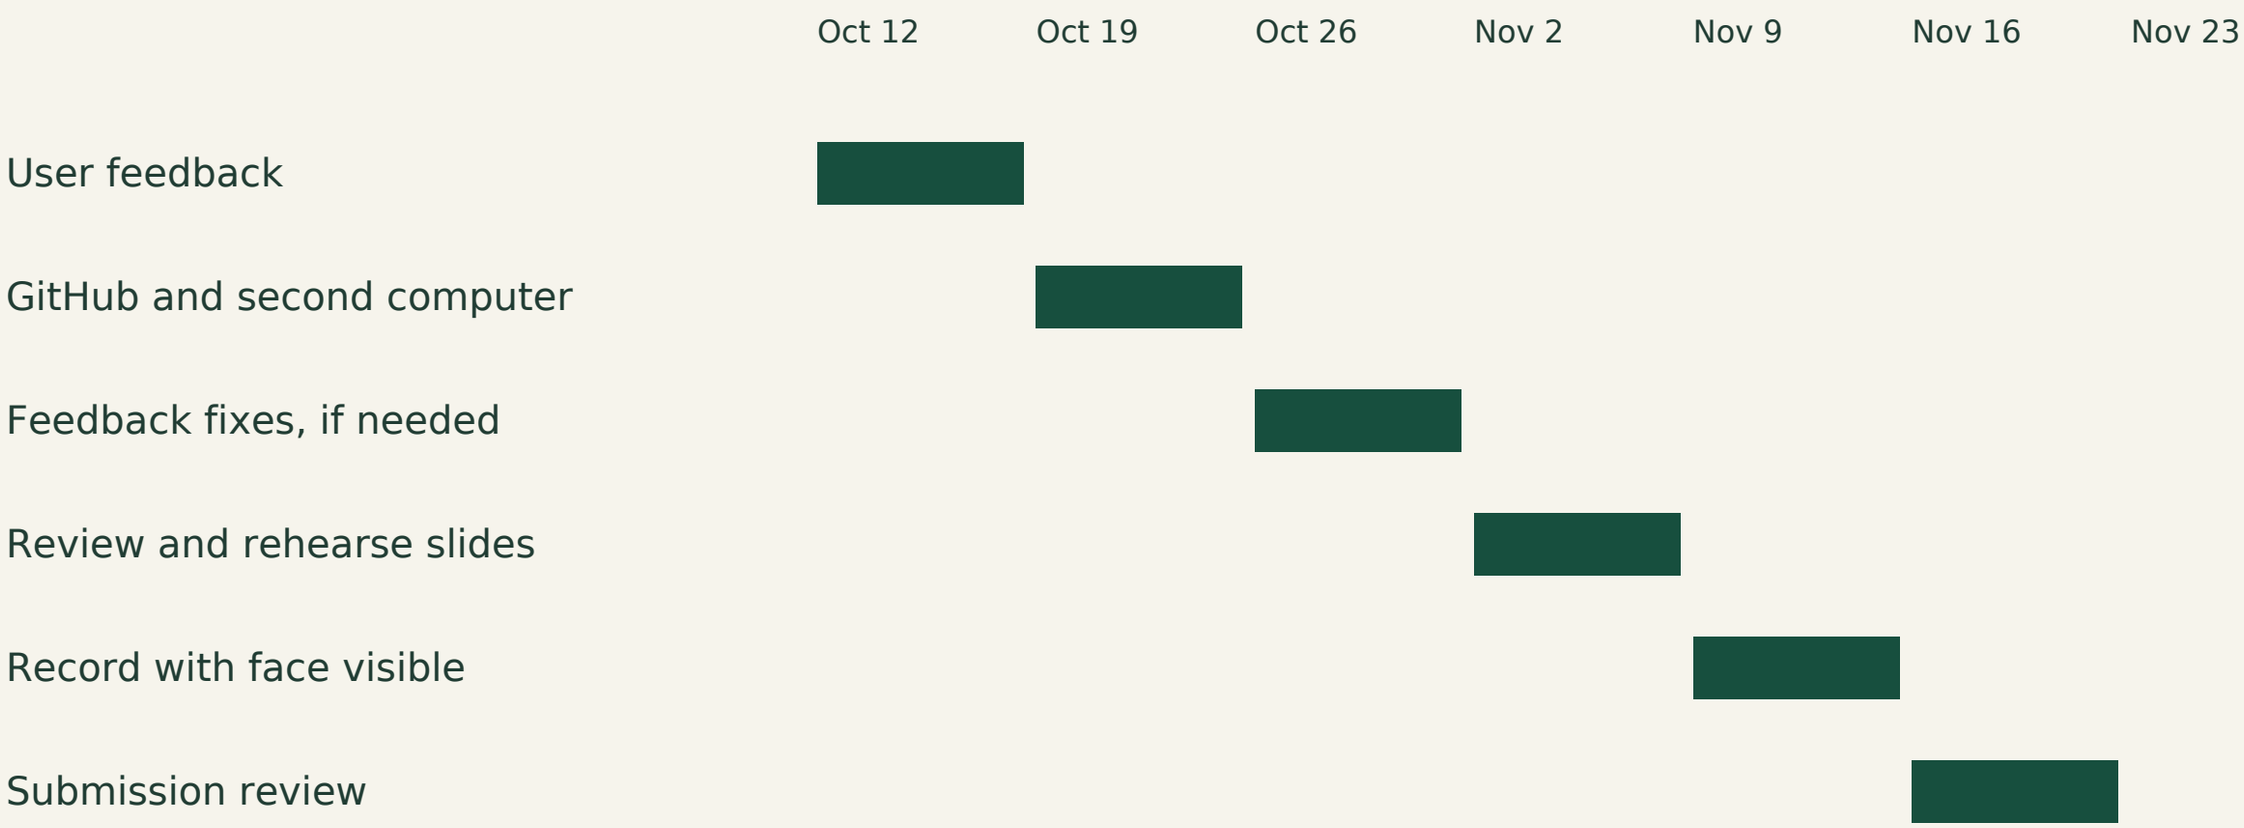

Target readiness: November 22, leaving time before a December deadline. Replan after the professor confirms the due date and after user feedback.

PERT: remaining work estimates

Sideline | Implementation snapshot: October 11, 2026

Estimates measure focused effort hours. Activities can span several calendar days. They are planning assumptions, not logged hours.

J. User acceptance: optimistic 2, most likely 4, pessimistic 6. Expected 4.00 hours.

K. Public repository and separate computer: 2, 3, 5. Expected 3.17 hours.

L. Recording: 1, 2, 3. Expected 2.00 hours.

M. Final submission review: 0.5, 1, 1.5. Expected 1.00 hour.

PERT expected effort = (optimistic + 4 × most likely + pessimistic) / 6.

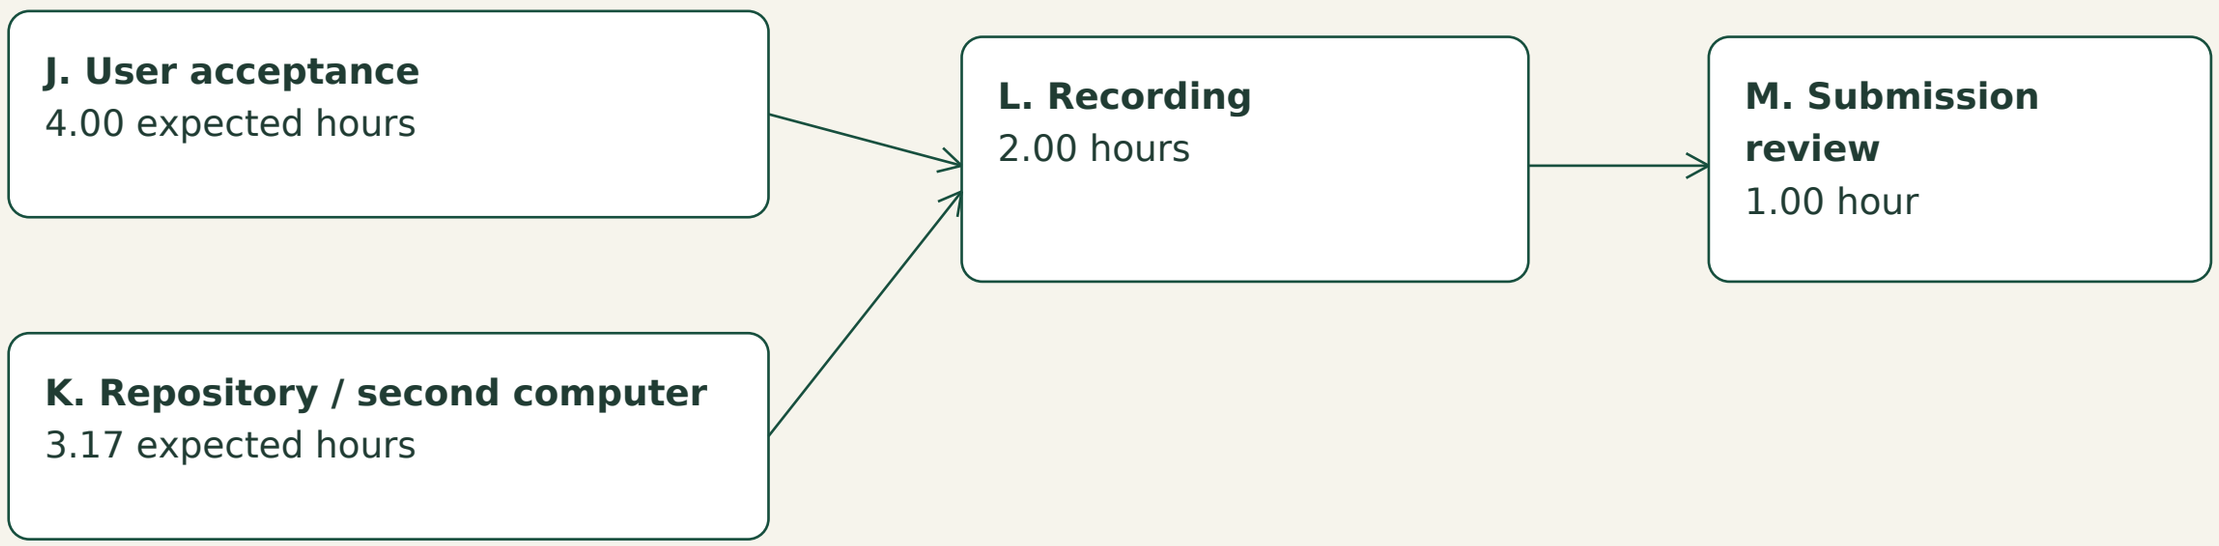

Critical path and dependencies

Sideline | Implementation snapshot: October 11, 2026

Both J and K must finish before recording L. Submission review M follows L. This network assumes slide review finishes in parallel and no additional model changes are required.

Remaining expected critical path: J → L → M = 4 + 2 + 1 = 7 focused hours. Alternate K → L → M = 6.17 hours. K has approximately 0.83 hours of modeled slack.

Critical-path variance: ((6−2)/6)² + ((3−1)/6)² + ((1.5−0.5)/6)² = 0.583 hours². Standard deviation ≈ 0.76 hours. These estimates do not provide a validated completion probability.

A single student may be unable to work J and K in parallel. The total expected remaining effort is 10.17 hours. Waiting for classmates, account setup or installing dependencies can extend calendar time.

Earlier completed dependency chain: data import → SQL → advanced features → model → Flask interface → local checks → evidence. Baseline development also follows SQL. Revisions may reopen completed tasks.
